




Lawrence Berkeley National Lab Capital Projects

Presentation to Community Advisory Group

June 15, 2015

Building Construction Map

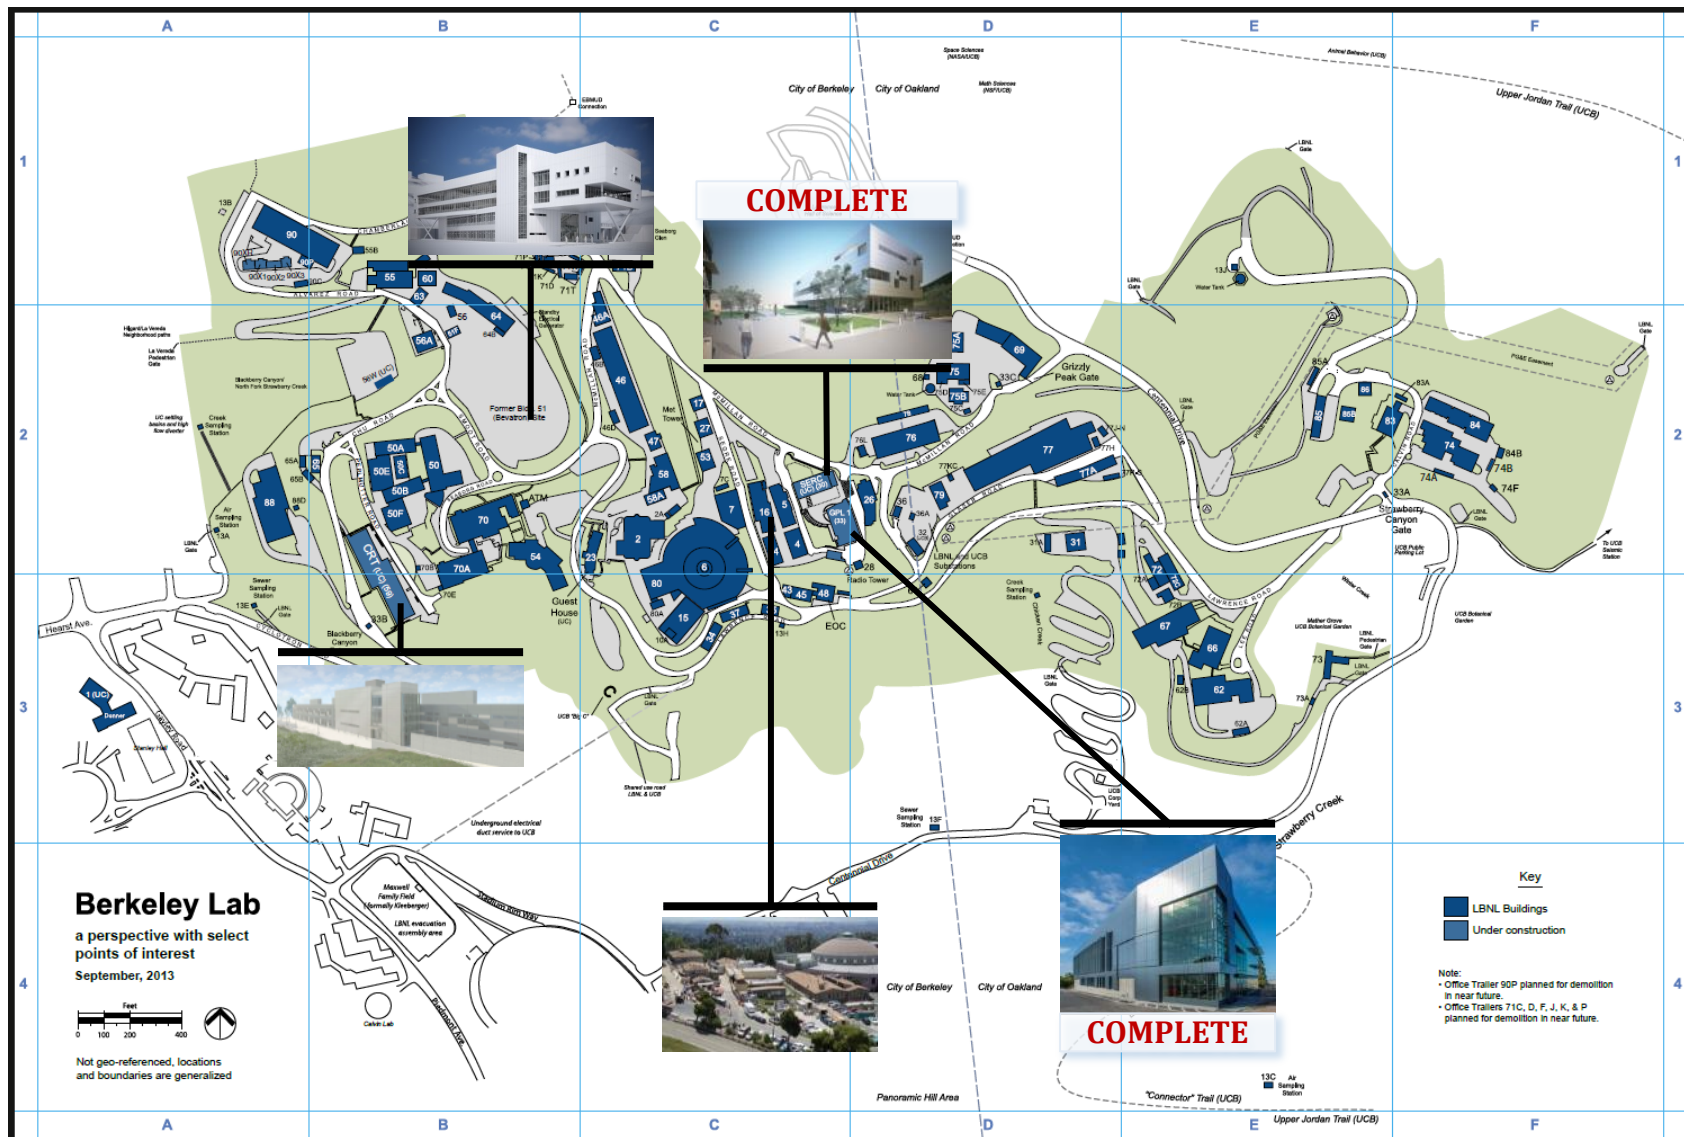

Solar Energy Research Center (SERC)



SERC – Current Activities



SERC – Current Activities




SERC – Current Activities



SERC – Current Activities



SERC – Current Activities

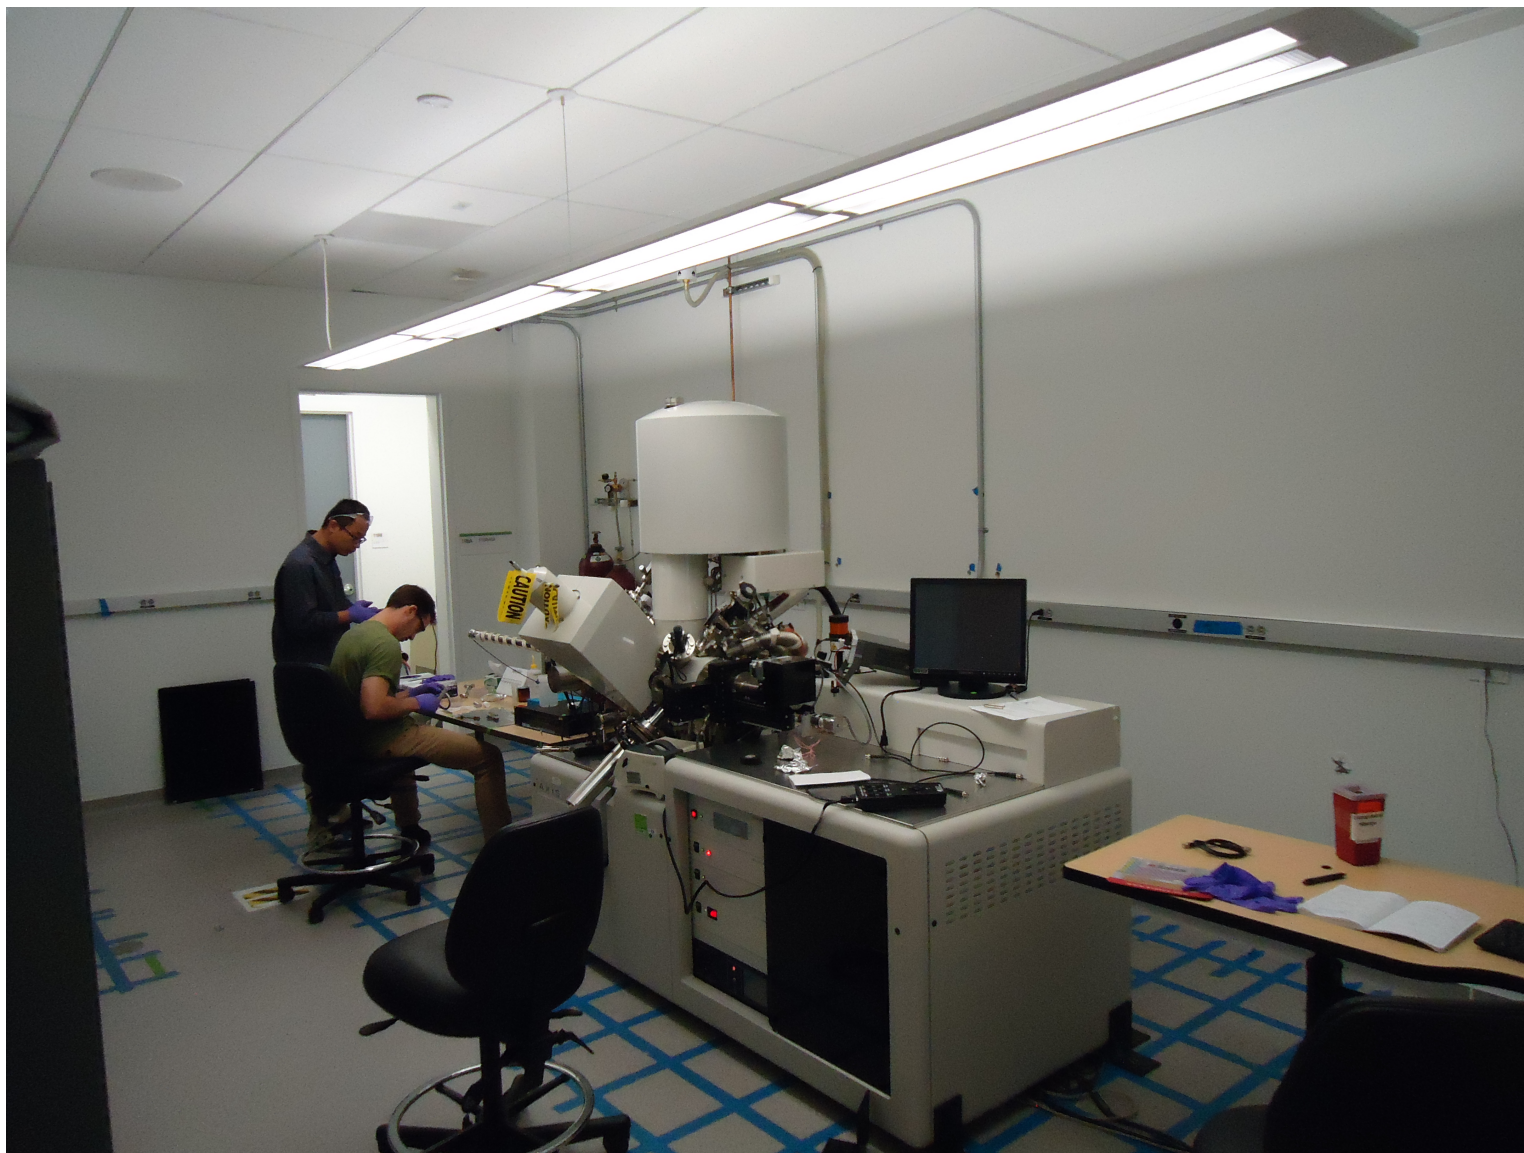

General Purpose Laboratory (GPL)



GPL – Current Activities



2015/06/15

GPL – Current Activities



GPL – Current Activities



GPL – Current Activities




GPL – Current Activities



Old Town Demolition (OTD)



Old Town Demolition (OTD)

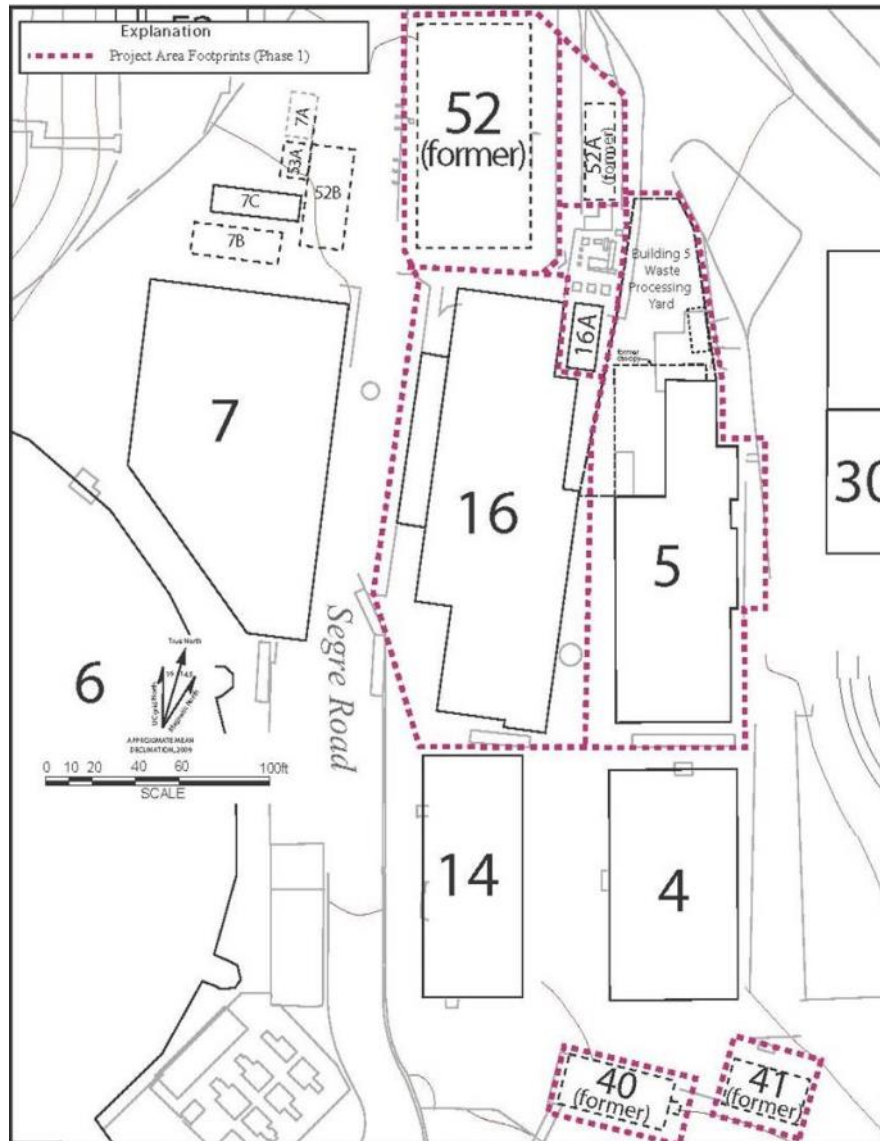


Location of Old Town Demolition Project Area (Phase 1)
- Buildings 5, 16, 16A, 40, 41, 52 and 52A.

Old Town Demolition (OTD)



- Demo subcontractor, Dynamic Management Solutions, LLC (DMS), issued Notice to Proceed with field work on 6/5/15.
- Will proceed with hazardous material abatement of buildings 5 and 16, demolition of buildings 5 and 16, then removal and cleanup of slabs and soils associated with 5, then 52/52A, 16/16A, finally 40/41.
- Current forecast schedule shows early finish date of February 16, 2016 and late finish date of May 16, 2016.

Integrative Genomics Building (IGB)

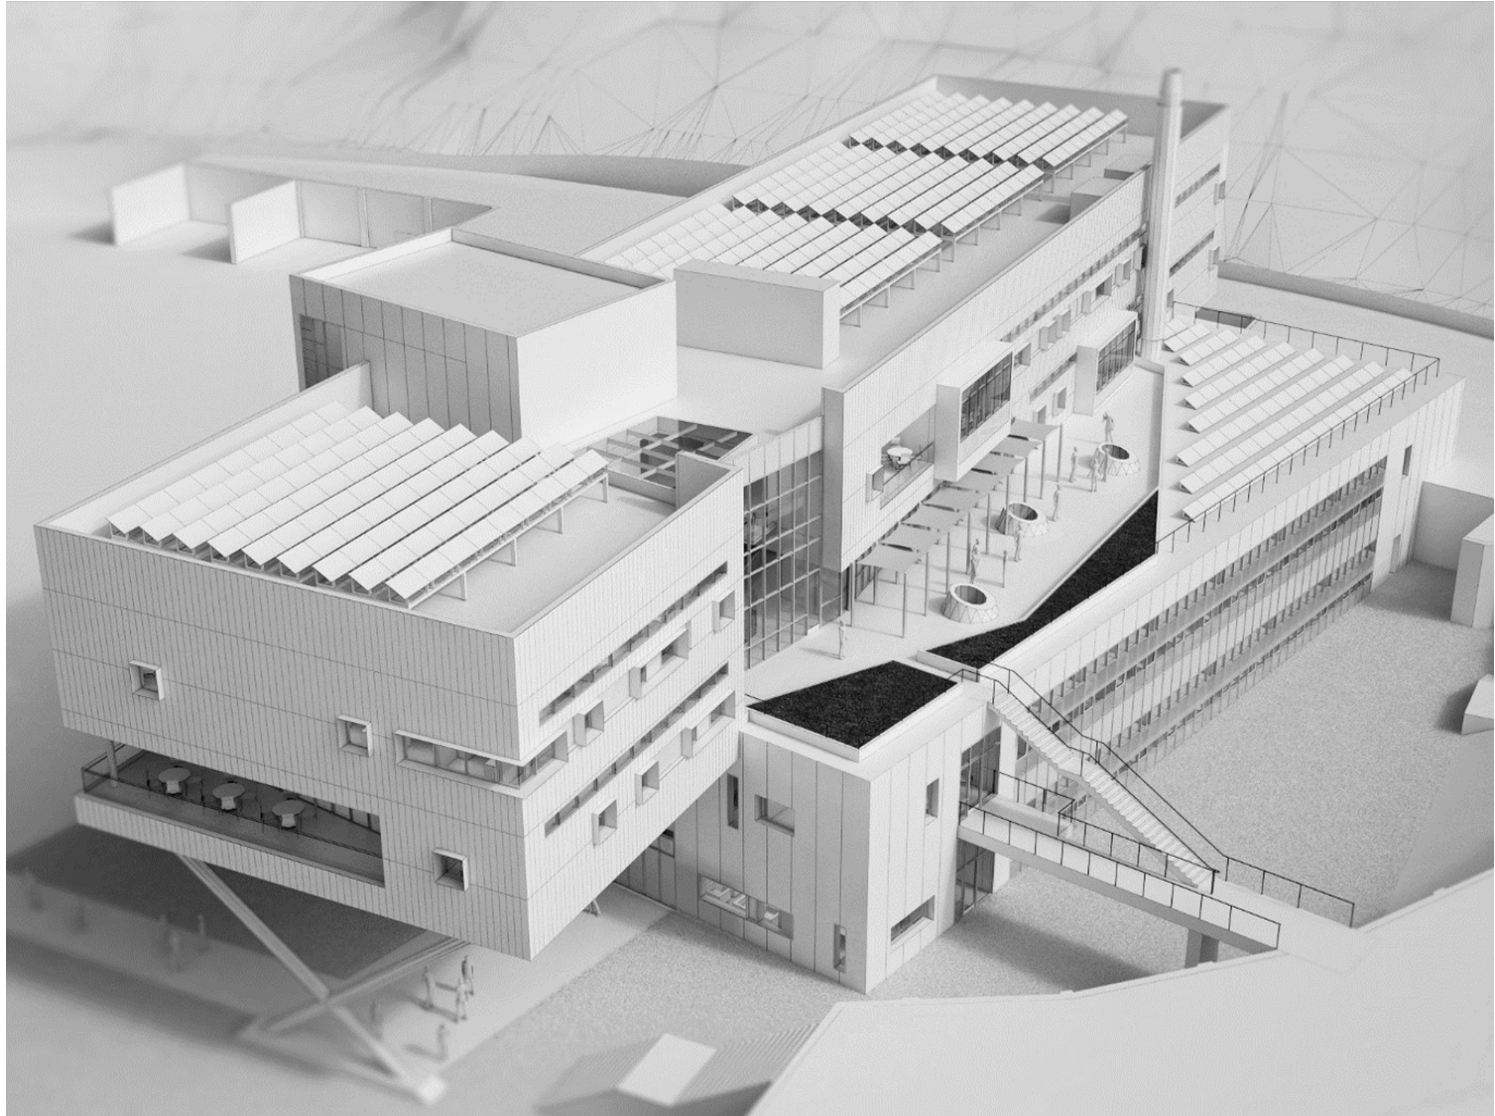



IGB –Current Activities



- Regents approved the design and CEQA document on June 12
- Schematic design is schedule for printing on June 25
- CM/GC proposal are being review with a selection to follow soon
- Anticipate design complete in the spring of 2016 with construction to start in the summer of 2016
- Construction to take 2.5 years completing approximately January 2019.



Thank You

Find us at: www.lbl.gov
